

Bryan Ellis presented a progress report from Innovative Construction Management on the Business Center and Arena. No action was taken.

Corey Alger came before the Board to discuss the change order for Building No. 4 of the Business Center. No action was taken.


**ORDER: APPROVE CHANGE ORDER NO. 1 FOR THE ARENA PROJECT IN THE
AMOUNT OF \$52,000**


Motion was made by Chad McLarty, duly seconded by Kevin Frye, to approve change order No. 1 for the Arena project in the amount of \$52,000.




The vote on the motion was as follows:

Supervisor Kevin Frye, voted yes
Supervisor Jeff Busby, voted yes
Supervisor David Rikard, voted yes
Supervisor Chad McLarty, voted yes
Supervisor Mike Roberts, voted yes

After the vote, President Busby, declared the motion carried, this the 18th day of June, 2018.


Jeff Busby, President
Board of Supervisors


Sherry Wall, Chancery Clerk



Lafayette County Business Center & Multi-purpose Arena

EXECUTIVE SUMMARY

Project Summary


Construction Progress

- Project NTP April 9, 2018
- Project Completion Date March 5, 2019
- Project Duration 330 Days
- Remaining Duration 266 Days
- Percent Complete (Calendar Days) 19%


Total Time Impacts

- Additional Contract Days Awarded 0 Calendar Days
- Actual Rain/Weather Days 8 Calendar Days


Business Center Milestone Progress




Business Center Submittal Progress

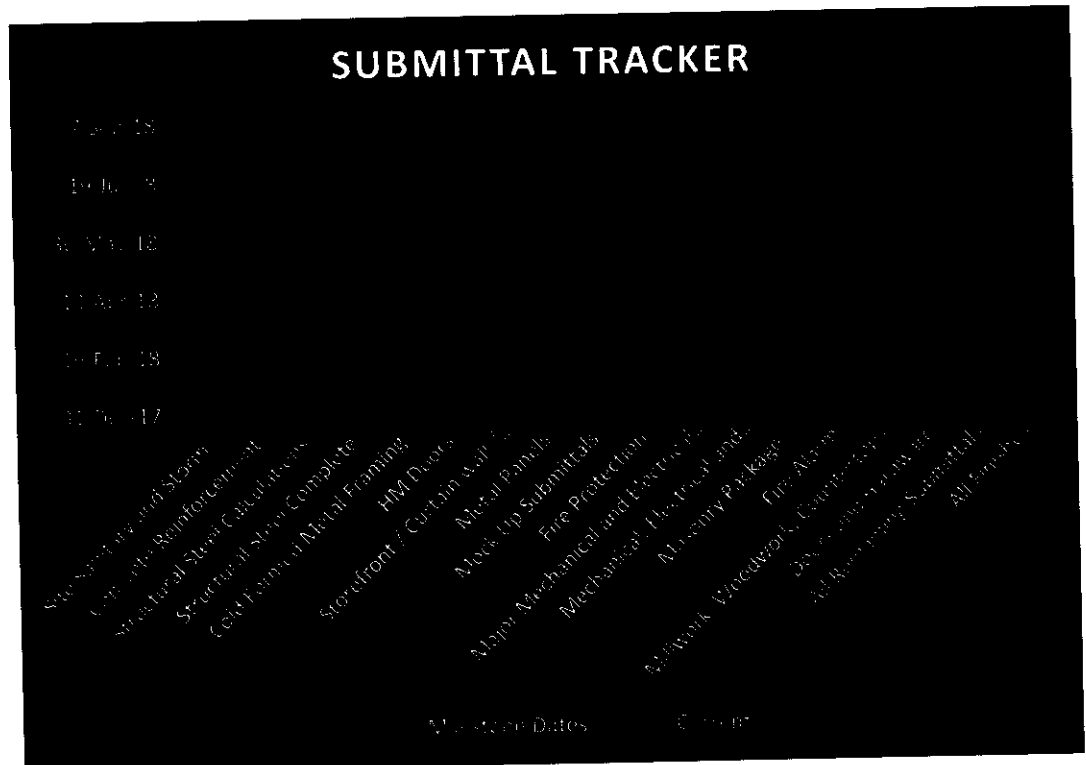

Arena Milestone Progress



Arena Submittal Progress

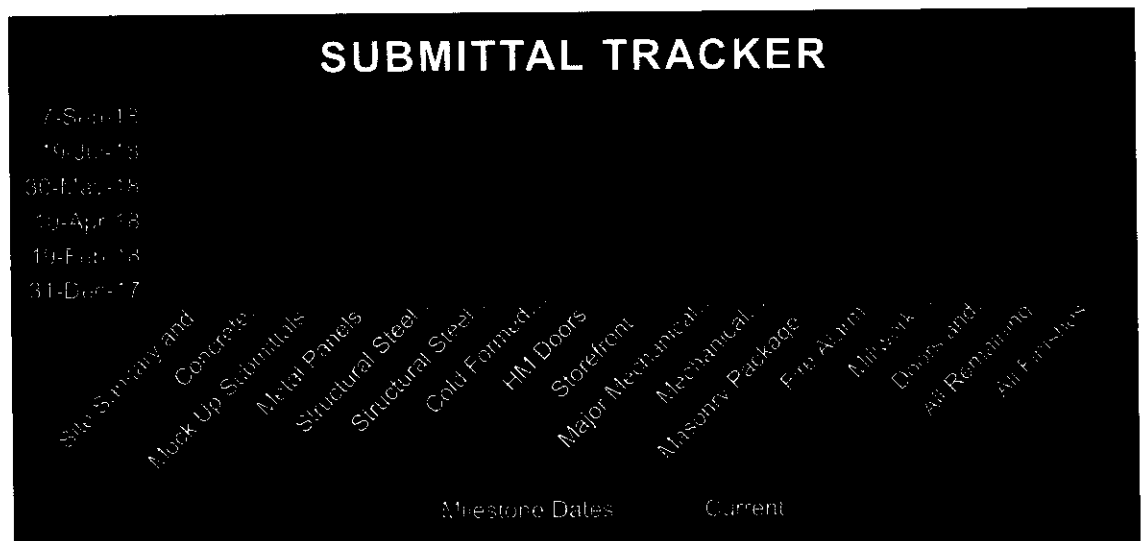

Project Tracking

Business Center Current Schedule Update as of 6.12.2018

Slab on Grade Building # 2: Complete 6/8

Underground P&E Building #1: Complete 6/8

Underground P&E Building #4: Start 6/11

Civil Sanitary Sewer: Complete 6/12

Arena Current Schedule Update as of 6.12.2018

Practice Arena Foundations: Complete 6/8

Practice Arena Structural Steel: Start 6/13

Site Storm Drainage System: Complete 6/8

Photos





6/11/2018

